




Interstate 405 Improvement Project Update



Project Location and Key Features

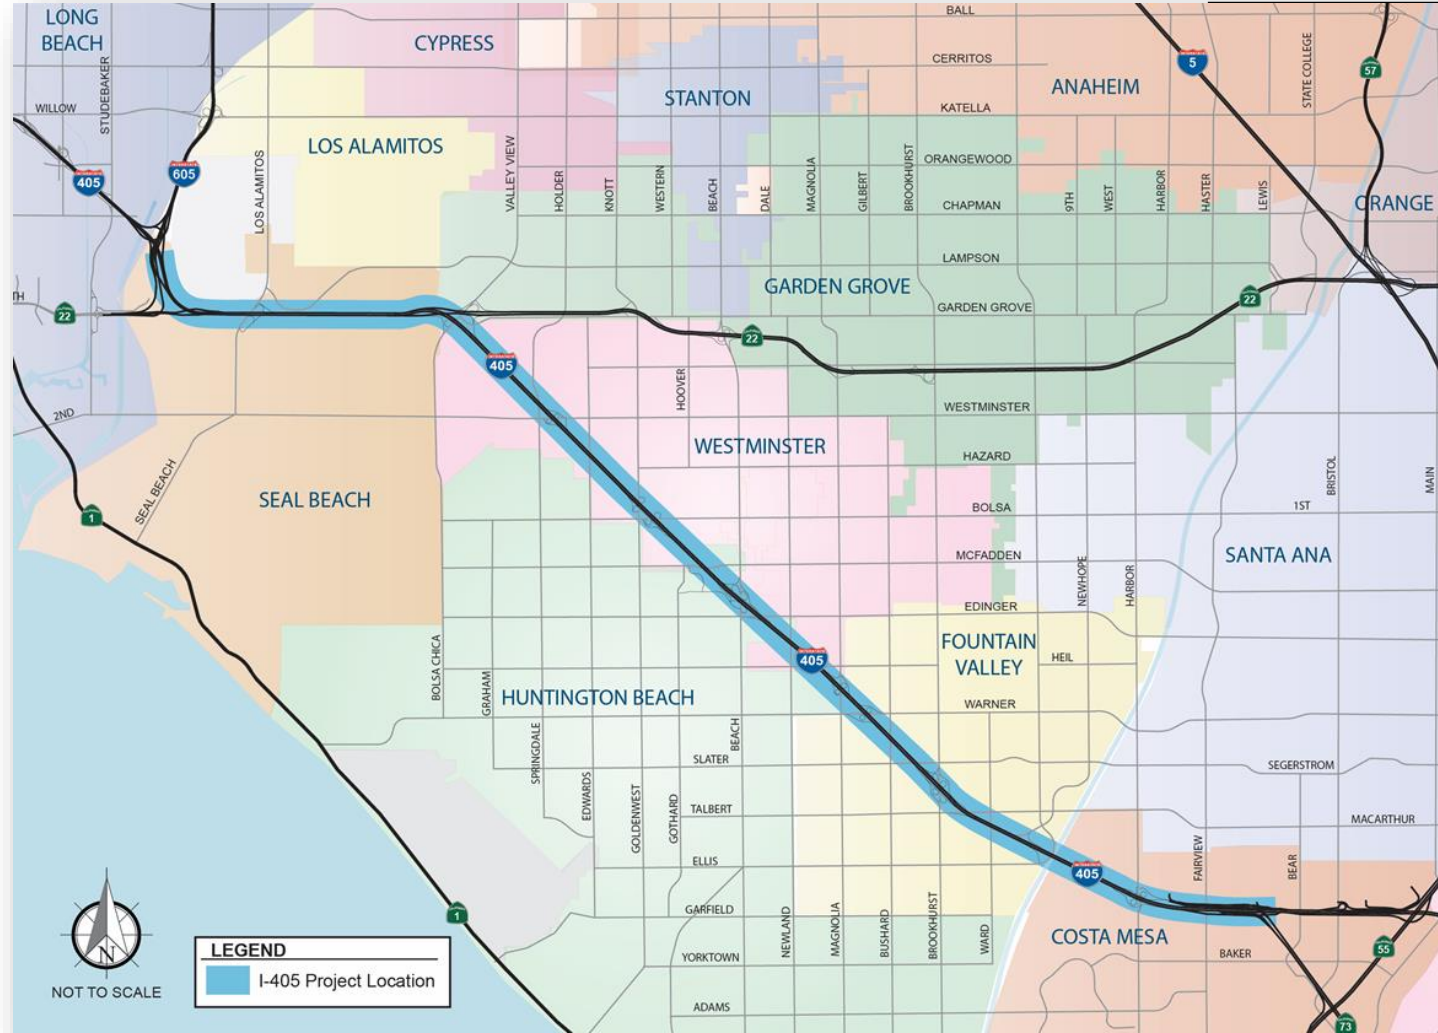

DB Project Update



General

- Over 95 percent complete with Interstate 405 (I-405) Improvement Project
- Remaining work consists of landscaping, additional bridge lighting, cultural resources restoration, and punch list activities

Construction

- All bridges complete
- All ramps complete
- All walls and paving complete

Construction Update



I-405/State Route 73 median connector bridge complete

Construction Update (Cont.)



Ward Street bridge complete

Construction Update (Cont.)




Warner Avenue bridge complete

Construction Update (Cont.)



Newland Street bridge complete

Bridge Construction Map

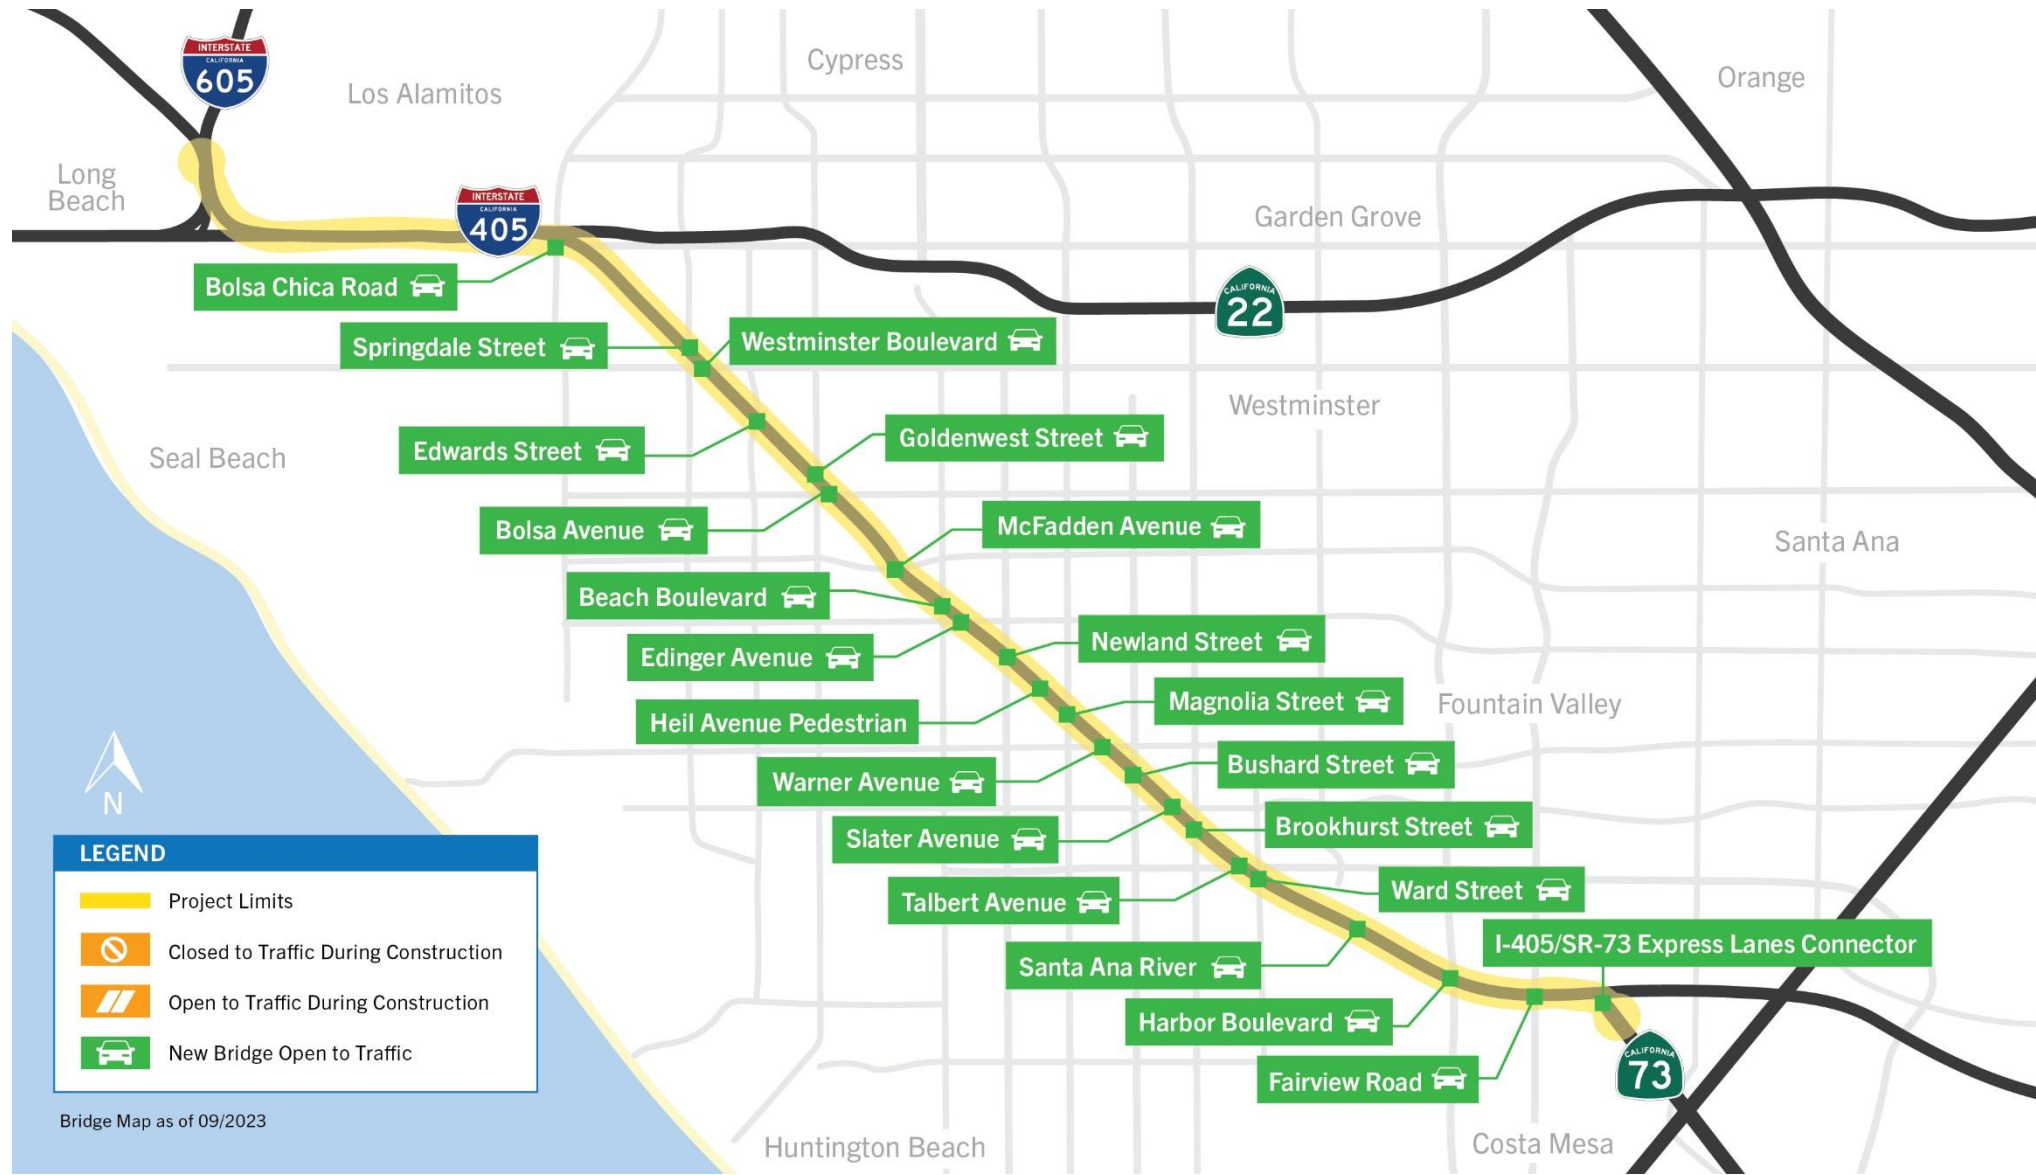

Bridge Map as of 09/2023

Express Lanes Update



Traffic Operations Center

- Tenant improvements completed
- Furniture and equipment installed
- Staffing being provided by Kapsch

Customer Service Center

- Tenant improvements completed
- Furniture and equipment installed
- Staffing being provided by WSP

Upcoming Agreements

- Enforcement services with the California Highway Patrol
- Maintenance agreement with the California Department of Transportation

Tolling Elements




405 Express Lanes tolling elements

Tolling Elements (Cont.)



Express Lanes striping

Tolling Elements (Cont.)

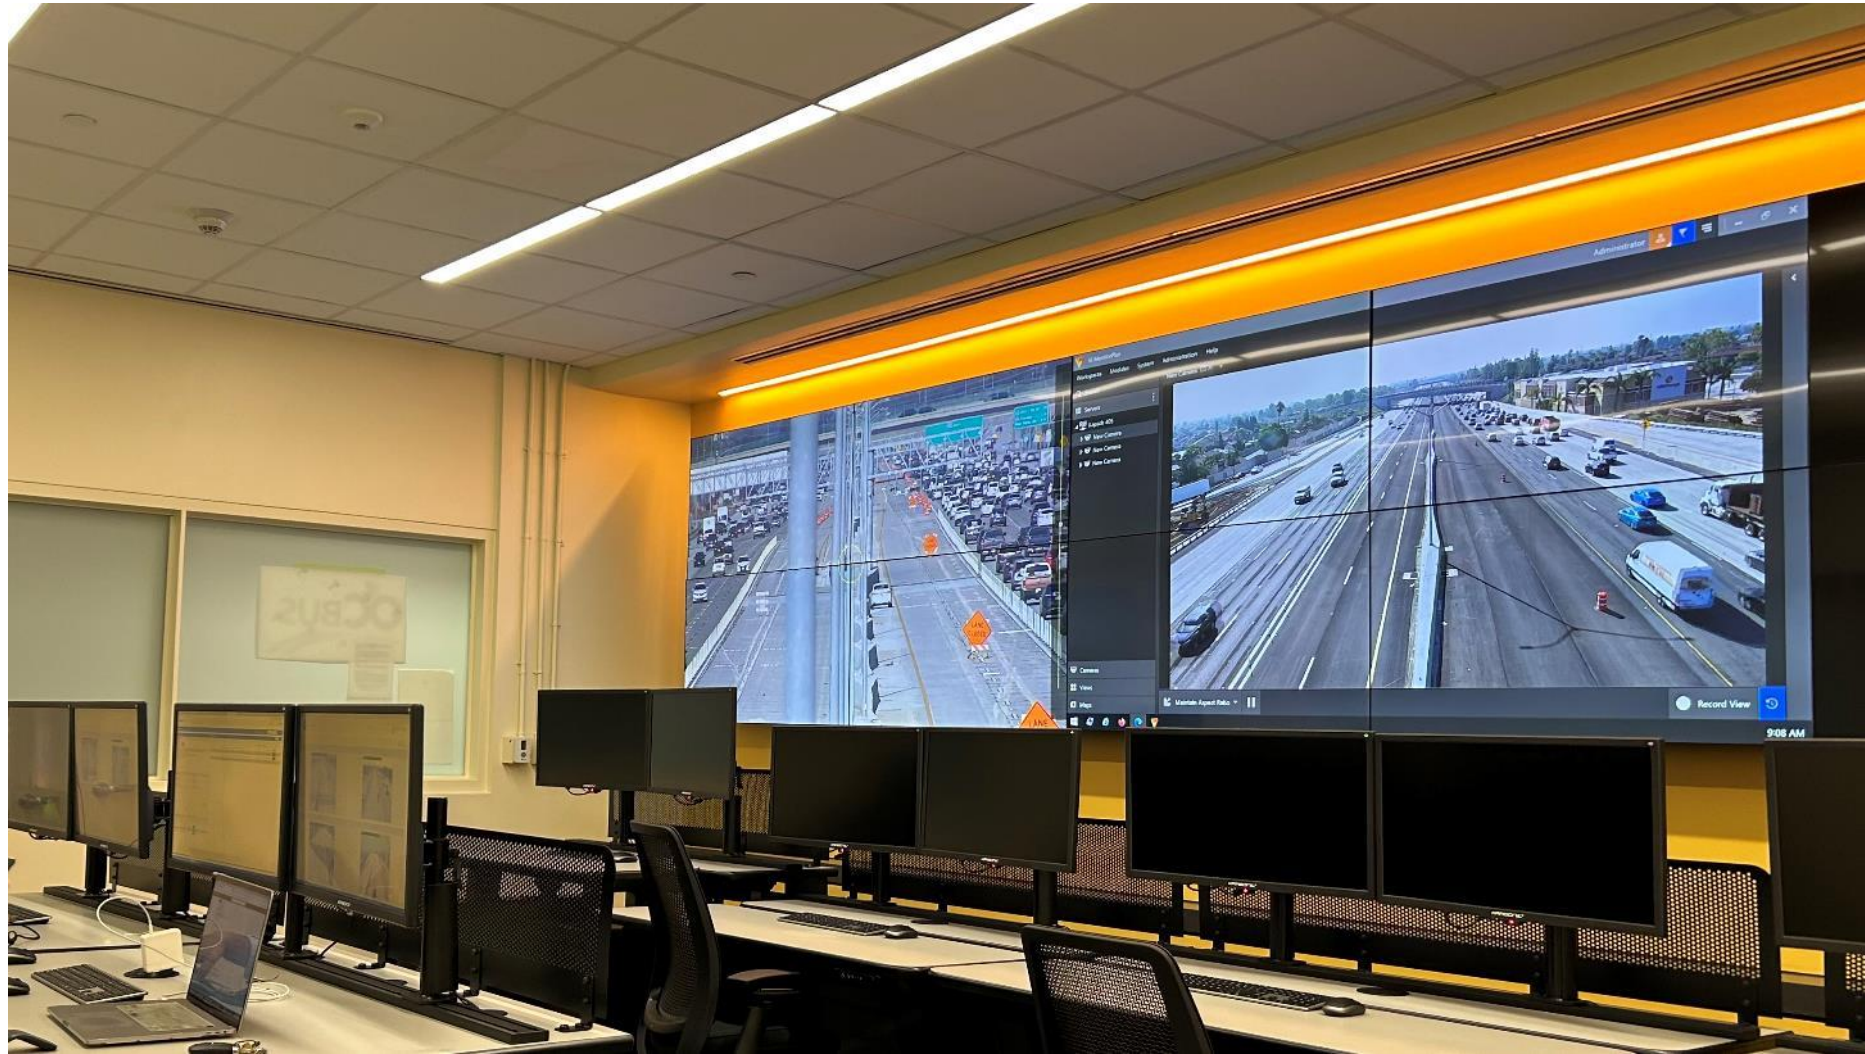

Traffic Operations Center at Santa Ana Bus Base

Next Steps



Milestone	Completion Date
Anticipated opening of all lanes	Late 2023
DB project completion (landscaping, installation of remaining bridge lighting, cultural resources restoration, and punch list activities will be ongoing until project completion)	February 2024
DB final acceptance (final punch list activities will be addressed and acceptance of project improvements by stakeholders, including Caltrans and the cities)	June 2024
DB contract acceptance (end of a three-year plant establishment period)	2027

Project Contact Information



405project@octa.net



888-400-8994 (English/Español)
888-662-6589 (Tiếng Việt)



octa.net/405improvement
405ExpressLanes.com



[/405improvement](https://www.facebook.com/405improvement)



[@405improvement](https://twitter.com/405improvement)



[@405_Improvement](https://www.instagram.com/405_Improvement)
